

Customer: Savills (UK) Limited

Job No: 108700

Job Title: *MF*Survey/tank empty

SLA:

Job Type: Planned Works

Site Group:

Site Address: Bucks Farm Barn

Cost Code:

Howe Lane

Binfield

Bracknell

RG42 5QS

Start Date: 03/03/2025 10:30

End Date: 03/03/2025 14:30

Cust Ref: Tom Eyston

Work Description:

The RFQ is following the request via email to attend site and conduct a survey of the drainage and septic tank to see if this conforms to standard.

We would recommend the septic tank to be emptied and have allowed for 2000g tanker to attend site, CCTV survey team with confined spaces if required to enter the tank to survey the drainage down to the septic tank and survey the inside of the tank to confirm outlet and if working.

Any issues found will be highlighted and recorded within the CCTV report and full recommendations and quotation for and remedial works will accompany the report. The below costs are based on half a day on-site and location of the tank within 60m of Tanker

Tom-07929089995

Our prices assume full unhindered access

free issue water supply

Free parking for vehicles.

W3W-bulky.banks.movie

Engineer Report:

Arrived on site and made contact with the site share holder.

After locating the tank and lifted the board off the chamber to find the Cess Pit was at full level. After locating the pit, set up the Suction Hose and emptied the Tank. Water ingress was back flowing in through the Outgoing 100mm Pipe as the Water Table is at high level.


The Tank has an INCOMING 100mm Pipe at high level. The Tank has a Dividing Wall Plate which is undamaged. CCTV Survey of Tank carried out and this showed that there was no other Infiltration located in the Tank. Upstream of the Tank is two INCOMING Manholes, CCTV Survey carried out on the main Line. Downstream of the Tank a 150mm Drop Pie in the ground but SURCHARGED holding water as high level Water Table. Map drawn up of the site and Site Left Safe and Secure.

Tanker attended site to empty a septic tank.

On arrival to site, located the tank and set up a safe area to work and emptied out 1000 gallons from the septic tank

Waste was then disposed of in a licensed facility and the WTN is attached for the report.

| H&S Pre-Work Checklist | Comments | Result |
|------------------------|----------|--------|
| | | |



Customer: Savills (UK) Limited

Job Title: *MF*Survey/tank empty

Job Type: Planned Works

Site Address: Bucks Farm Barn
Howe Lane
Binfield
Bracknell
RG42 5QS

Job No: 108700

SLA:

Site Group:




Cost Code:

Start Date: 03/03/2025 10:30

End Date: 03/03/2025 14:30

Cust Ref: Tom Eyston

| H&S Pre-Work Checklist | Comments | Result |
|--|----------|--------|
| You have read and understood the description of works? | | Yes |
| Ensure work area is made safe | | Yes |
| Carry out a Point of Work Assessment (Dynamic RA) | | Yes |
| Wear appropriate PPE | | Yes |
| Inspect RAMS for the task | | Yes |
| Read and understand any drawings provided | | Yes |
| Check equipment you will use is safe and fit for purpose | | Yes |
| Log any hazards and feedback immediately to HSEQ Manager, Line Manager and Client/Customer | | Yes |
| You are fully trained, equipped & competent to carry out the works? | | Yes |

| Description | Images |
|--------------------------------------|---|
| Linked folder | |
| MH2 location view |  |
| sample point pipe |  |
| Tanker on site taking down levels .. |  |
| | |



Customer: Savills (UK) Limited

Job Title: *MF*Survey/tank empty

Job Type: Planned Works

Site Address: Bucks Farm Barn
Howe Lane
Binfield
Bracknell
RG42 5QS

Job No: 108700

SLA:






Site Group:


Cost Code:

Start Date: 03/03/2025 10:30

End Date: 03/03/2025 14:30

Cust Ref: Tom Eyston

| Description | Images |
|------------------------------------|---|
| cess pit incoming pipe |  |
| site set up for cess pit |  |
| MH2 location |  |
| cess pit and sample point location |  |
| Cess pit vent pipe |  |



Customer: Savills (UK) Limited

Job Title: *MF*Survey/tank empty

Job Type: Planned Works

Site Address: Bucks Farm Barn
Howe Lane
Binfield
Bracknell
RG42 5QS

Job No: 108700

SLA:

Site Group:

Cost Code:

Start Date: 03/03/2025 10:30

End Date: 03/03/2025 14:30

Cust Ref: Tom Eyston

| Description | Images |
|---------------------------------------|--------|
| MH1 General view | |
| cess pit outgoing pipe with back flow | |
| MH1 Location | |
| cess pit empty | |
| site glass on tanker | |



Customer: Savills (UK) Limited

Job Title: *MF*Survey/tank empty

Job Type: Planned Works

Site Address: Bucks Farm Barn

Howe Lane

Binfield

Bracknell

RG42 5QS

Job No: 108700

SLA:


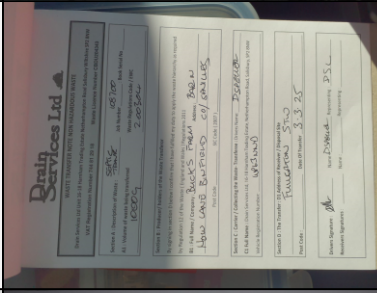
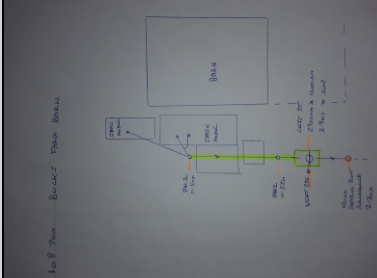
Site Group:

Cost Code:

Start Date: 03/03/2025 10:30

End Date: 03/03/2025 14:30

Cust Ref: Tom Eyston

| Description | Images |
|-------------------|---|
| Cess pit full |  |
| WTN |  |
| CCTV Site mapping |  |

Engineer/Customer signatures:
